



325-829-0146

www.rennerinspectionsservices.com
david@rennerinspectionsservices.com



INSPECTED FOR

David Taylor
816 E 6th St
Baird, TX 79504

February 26, 2018

PROPERTY INSPECTION REPORT

Prepared For: David Taylor
(Name of Client)

Concerning: 816 E 6th St, Baird, TX 79504
(Address or Other Identification of Inspected Property)

By: River Dillard, Lic #22970 02/26/2018
(Name and License Number of Inspector) (Date)

PURPOSE, LIMITATIONS AND INSPECTOR / CLIENT RESPONSIBILITIES

This property inspection report may include an inspection agreement (contract), addenda, and other information related to property conditions. If any item or comment is unclear, you should ask the inspector to clarify the findings. It is important that you carefully read ALL of this information.

This inspection is subject to the rules ("Rules") of the Texas Real Estate Commission ("TREC"), which can be found at www.trec.texas.gov.

The TREC Standards of Practice (Sections 535.227-535.233 of the Rules) are the minimum standards for inspections by TREC-licensed inspectors. An inspection addresses only those components and conditions that are present, visible, and accessible at the time of the inspection. While there may be other parts, components or systems present, only those items specifically noted as being inspected were inspected. The inspector is NOT required to turn on decommissioned equipment, systems, utility services or apply an open flame or light a pilot to operate any appliance. The inspector is NOT required to climb over obstacles, move furnishings or stored items. The inspection report may address issues that are code-based or may refer to a particular code; however, this is NOT a code compliance inspection and does NOT verify compliance with manufacturer's installation instructions. The inspection does NOT imply insurability or warrantability of the structure or its components. Although some safety issues may be addressed in this report, this inspection is NOT a safety/code inspection, and the inspector is NOT required to identify all potential hazards.

In this report, the inspector shall indicate, by checking the appropriate boxes on the form, whether each item was inspected, not inspected, not present or deficient and explain the findings in the corresponding section in the body of the report form. The inspector must check the Deficient (D) box if a condition exists that adversely and materially affects the performance of a system or component or constitutes a hazard to life, limb or property as specified by the TREC Standards of Practice. General deficiencies include inoperability, material distress, water penetration, damage, deterioration, missing components, and unsuitable installation. Comments may be provided by the inspector whether or not an item is deemed deficient. The inspector is not required to prioritize or emphasize the importance of one deficiency over another.

Some items reported may be considered life-safety upgrades to the property. For more information, refer to Texas Real Estate Consumer Notice Concerning Recognized Hazards or Deficiencies below.

THIS PROPERTY INSPECTION IS NOT A TECHNICALLY EXHAUSTIVE INSPECTION OF THE STRUCTURE, SYSTEMS OR COMPONENTS. The inspection may not reveal all deficiencies. A real estate inspection helps to reduce some of the risk involved in purchasing a home, but it cannot eliminate these risks, nor can the inspection anticipate future events or changes in performance due to changes in use or occupancy. It is recommended that you obtain as much information as is available about this property, including any seller's disclosures, previous inspection reports, engineering reports, building/remodeling permits, and reports performed for or by relocation companies, municipal inspection departments, lenders, insurers, and appraisers. You should also attempt to determine whether repairs, renovation, remodeling, additions, or other such activities have taken place at this property. It is not the inspector's responsibility to confirm that information obtained from these sources is complete or accurate or that this inspection is consistent with the opinions expressed in previous or future reports.

ITEMS IDENTIFIED IN THE REPORT DO NOT OBLIGATE ANY PARTY TO MAKE REPAIRS OR TAKE OTHER ACTIONS, NOR IS THE PURCHASER REQUIRED TO REQUEST THAT THE SELLER TAKE ANY ACTION. When a deficiency is reported, it is the client's responsibility to obtain further evaluations and/or cost estimates from qualified service professionals. Any such follow-up should take place prior to the expiration of any time limitations such as option periods. Evaluations by qualified tradesmen may lead to the discovery of additional deficiencies which may involve additional repair costs. Failure to address deficiencies or comments noted in this report may lead to further damage of the structure or systems and add to the original repair costs. The inspector is not required to provide follow-up services to verify that proper repairs have been made.

Property conditions change with time and use. For example, mechanical devices can fail at any time, plumbing gaskets and seals may crack if the appliance or plumbing fixture is not used often, roof leaks can occur at any time regardless of the apparent condition of the roof, and the performance of the structure and the systems may change due to changes in use or occupancy, effects of weather, etc. These changes or repairs made to the structure after the inspection may render information contained herein obsolete or invalid. This report is provided for the specific benefit of the client named above and is based on observations at the time of the inspection. If you did not hire the inspector yourself, reliance on this report may provide incomplete or outdated information. Repairs, professional opinions or additional inspection reports may affect the meaning of the information in this report. It is recommended that you hire a licensed inspector to perform an inspection to meet your specific needs and to provide you with current information concerning this property.

TEXAS REAL ESTATE CONSUMER NOTICE CONCERNING HAZARDS OR DEFICIENCIES

Each year, Texans sustain property damage and are injured by accidents in the home. While some accidents may not be avoidable, many other accidents, injuries, and deaths may be avoided through the identification and repair of certain hazardous conditions. Examples of such hazards include:

- malfunctioning, improperly installed or missing ground fault circuit protection (GFCI) devices for electrical receptacles in garages, bathroom, kitchens, and exterior areas;
- malfunctioning arc fault protection (AFCI) devices;
- ordinary glass in locations where modern construction techniques call for safety glass;
- malfunctioning or lack of fire safety features such as, smoke alarms, fire-rated doors in certain locations, and functional emergency escape and rescue openings in bedrooms;
- malfunctioning carbon monoxide alarms;
- excessive spacing between balusters on stairways and porches;
- improperly installed appliances;
- improperly installed or defective safety devices;
- lack of electrical bonding and grounding; and
- lack of bonding on gas piping, including corrugated stainless steel tubing (CSST).

To ensure that consumers are informed of hazards such as these, the Texas Real Estate Commission (TREC) has adopted Standards of Practice requiring licensed inspectors to report these conditions as "Deficient" when performing an inspection for a buyer or seller, if they can be reasonably determined.

These conditions may not have violated building codes or common practices at the time of the construction of the home, or they may have been "grandfathered" because they were present prior to the adoption of codes prohibiting such conditions. While the TREC Standards of Practice do not require inspectors to perform a code compliance inspection, TREC considers the potential for injury or property loss from the hazards addressed in the Standards of Practice to be significant enough to warrant this notice.

Contract forms developed by TREC for use by its real estate licensees also inform the buyer of the right to have the home inspected and can provide an option clause permitting the buyer to terminate the contract within a specified time. Neither the Standards of Practice nor the TREC contract forms requires a seller to remedy conditions revealed by an inspection. The decision to correct a hazard or any deficiency identified in an inspection report is left to the parties to the contract for the sale or purchase of the home.

INFORMATION INCLUDED UNDER "ADDITIONAL INFORMATION PROVIDED BY INSPECTOR", OR PROVIDED AS AN ATTACHMENT WITH THE STANDARD FORM, IS NOT REQUIRED BY THE COMMISSION AND MAY CONTAIN CONTRACTUAL TERMS BETWEEN THE INSPECTOR AND YOU, AS THE CLIENT. THE COMMISSION DOES NOT REGULATE CONTRACTUAL TERMS BETWEEN PARTIES. IF YOU DO NOT UNDERSTAND THE EFFECT OF ANY CONTRACTUAL TERM CONTAINED IN THIS SECTION OR ANY ATTACHMENTS, CONSULT AN ATTORNEY.

ADDITIONAL INFORMATION PROVIDED BY INSPECTOR

Inspection Time In: **8:30 am** Time Out: **10:30 am** Property was: **Occupied**

Building Orientation (For Purpose Of This Report Front Faces): **South**

Weather Conditions During Inspection: **Sunny**

Outside temperature during inspection: **40 to 50 Degrees**

Parties present at inspection: **No other parties present during inspection.**

This report contains technical information. If you were not present during this inspection, please call the office to arrange for a consultation with your inspector. If you choose not to consult with the inspector, this inspection company cannot be held liable for your understanding or misunderstanding of the reports content.

The digital pictures in this report are a sample of the damages in place and should not be considered to show all of the damages and/or deficiencies found. There will be some damage and/or deficiencies not represented with digital imaging.

THIS REPORT IS PAID AND PREPARED FOR THE EXCLUSIVE USE BY David Taylor. THIS COPYRIGHTED REPORT IS NOT VALID WITHOUT THE SIGNED INSPECTION AGREEMENT.

THIS REPORT IS NOT TRANSFERABLE FROM THE CLIENT NAMED ABOVE

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I NI NP D

I. STRUCTURAL SYSTEMS

A. Foundations

Type of Foundation(s): Slab on Ground

Comments:

Foundation Is Performing Adequately

In my opinion, the foundation appears to be providing adequate support for the structure at the time of this inspection. I did not observe any apparent evidence that would indicate the presence of adverse performance or significant deficiencies in the foundation. The interior and exterior stress indicators showed little effects of adverse performance and I perceived the foundation to contain no significant unlevelness after walking the 1st level floors.

Foundation Maintenance & Care

- **Note:** Proper drainage and moisture control is needed with all foundation types. Due to the expansive nature of the load bearing soils in the area it is important to direct water away from the foundation at all locations and that the soil moisture content be maintained at a constant level around the structure. Improper drainage and moisture control may contribute to greater than normal foundation movement.

B. Grading and Drainage

Comments:

- Poor to negative site drainage was observed on the north and east sides of the structure. Proper drainage is needed to help prevent water from standing and/or ponding next to the foundation beam. Corrective measures may be needed if the water stands within 10-feet of the foundation perimeter beam for more than 24-hours.
- The soil line is too high on the north, east, west and south sides of the structure. Under current building standards there should be at least 4-inches of foundation visible below masonry veneer and 6-inches of foundation visible below wood type veneer.



I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I	NI	NP	D
---	----	----	---



-
-
-
-

C. Roof Covering Materials

Type(s) of Roof Covering: Metal

Viewed From: Walked on roof


Comments:

Roof Covering

All components were found to be performing and in satisfactory condition on the day of the inspection.

Flashing Details

All components were found to be performing and in satisfactory condition on the day of the inspection.

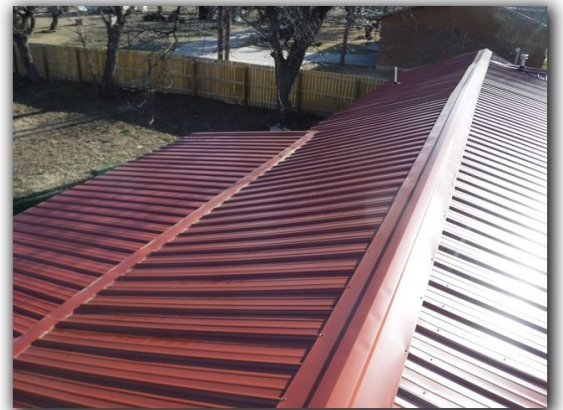

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I	NI	NP	D
---	----	----	---

D. Roof Structures and Attics

Viewed From: From Interior of Attic

Approximate Average Depth of Insulation: 4" to 6"

Approximate Average Thickness of Vertical Insulation: N/A

(Note: Recommended depth of attic floor insulation is approx. 10+ inches to achieve a R30 rating.)

Insulation Type: Batt or Blanket

Description of Roof Structure: Rafter Assembly

Attic Accessibility: Partial

Comments:

Roof Structure


All components were found to be performing and in satisfactory condition on the day of the inspection.

Attic Ventilation

All components were found to be performing and in satisfactory condition on the day of the inspection.

Attic Insulation

All components were found to be performing and in satisfactory condition on the day of the inspection.

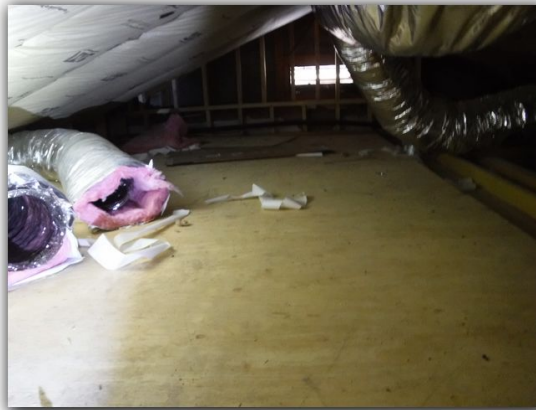

E. Walls (Interior and Exterior)

Description of Exterior Cladding: Hard Coat Stucco

Comments:

Interior Walls & Surfaces

- **Note:** There is evidence of painting and patching to the interior finish and prior interior finish repairs. This condition could limit the Inspectors visual observations and ability to render accurate opinions as to the performance of the structure.
- The tape lines are pulling and/or twisting in the wall intersections in the master bedroom. This condition is sometimes related to adverse foundation performance and should be further evaluated.
- Interior wall cracks were observed in the dining room, this could be the result of water penetration into the wall from the metal valley flashing area.

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient



I NI NP D

Stucco (Hard Coat or EIFS) Observation and Opinions

There is a stucco type product installed as the exterior veneer / cladding for this structure. Due to the known general misapplication of residential stucco products, associated deficiencies and water intrusion problems; full evaluation of this product requires a specialty inspection from a Properly Certified Third Party Stucco Inspector.

At this time a general limited visually based survey of the accessible exterior stucco veneer / cladding will be performed without the use of any specialized tools or procedures. The Inspectors findings will be listed below but all possible deficiencies will not be limited to the following:

- The exterior stucco type veneer/cladding has inadequate clearance from the finished grade (ground). Most manufacturers require a minimum of 4- to 6-inches of clearance from the finished grade (ground).
- Cracking of the stucco type veneer/cladding was observed on the north side of the structure. This condition should be further evaluated and corrected as necessary.
- Some deterioration and/or damage to the stucco type veneer/cladding was observed on the west side of the structure.

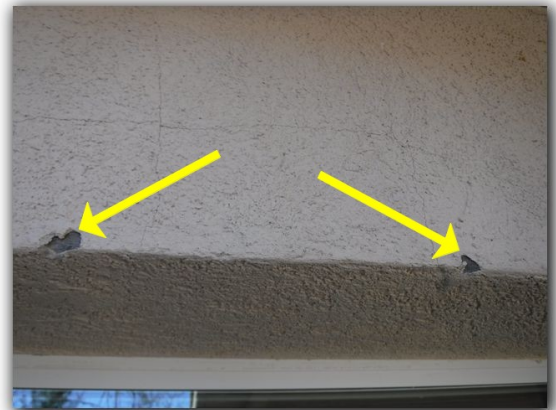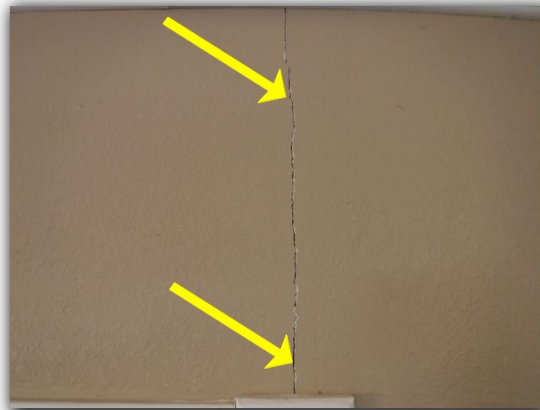

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I	NI	NP	D
---	----	----	---



F. Ceilings and Floors

Comments:

Ceilings

All components were found to be performing and in satisfactory condition on the day of the inspection.

Floors

- **Note:** The floors were observed to be out-of-level in some areas of the house.



G. Doors (Interior and Exterior)

Comments:

Interior Doors

All components were found to be performing and in satisfactory condition on the day of the inspection.

Exterior Doors

All components were found to be performing and in satisfactory condition on the day of the inspection.

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I	NI	NP	D
---	----	----	---

-

H. Windows

Comments:

Window Screens

- One or more of the window screens were observed to be damaged.
- One or more of the window screens were observed to be missing.

Windows

All components were found to be performing and in satisfactory condition on the day of the inspection.



-

I. Stairways (Interior and Exterior)

Comments:

-

J. Fireplaces and Chimneys

Comments:

-

K. Porches, Balconies, Decks, and Carports

Comments:

All components were found to be performing and in satisfactory condition on the day of the inspection.

-

L. Other

Comments:

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I	NI	NP	D
---	----	----	---

II. ELECTRICAL SYSTEMS

A. Service Entrance and Panels

Panel Box


Box Rating and/or Main Disconnect Rating: 200 amps

Box Location: East Exterior Wall

Cabinet Manufacturer: EATON

Comments:

All components were found to be performing and in satisfactory condition on the day of the inspection.

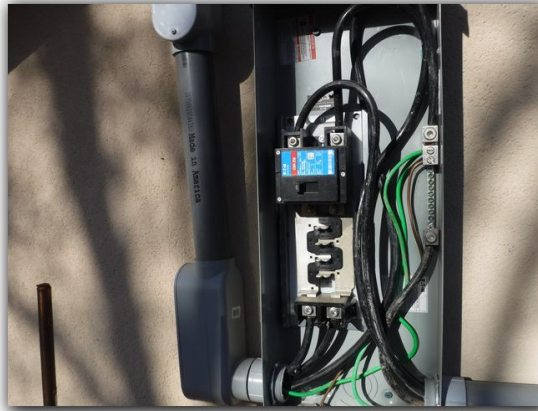


Sub Panel

Box Location: Laundry Room

Cabinet Manufacturer: General Electric - GE

Comments:

All components were found to be performing and in satisfactory condition on the day of the inspection.

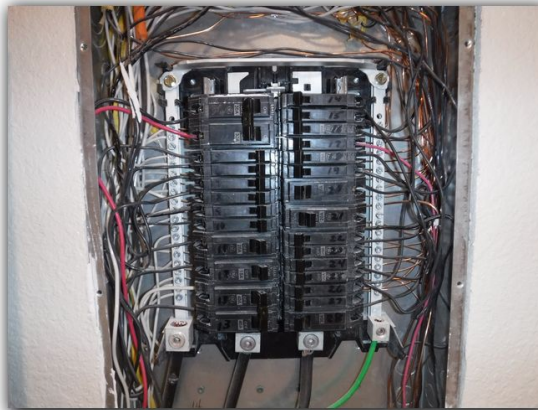

I=Inspected

NI=Not Inspected


NP=Not Present

D=Deficient

I	NI	NP	D
---	----	----	---

Service Entrance

- The electrical service wires hang to low over the roof structure. The electrical service wires from the service pole to the structure should clear all roof structure components by a minimum of 3-feet.

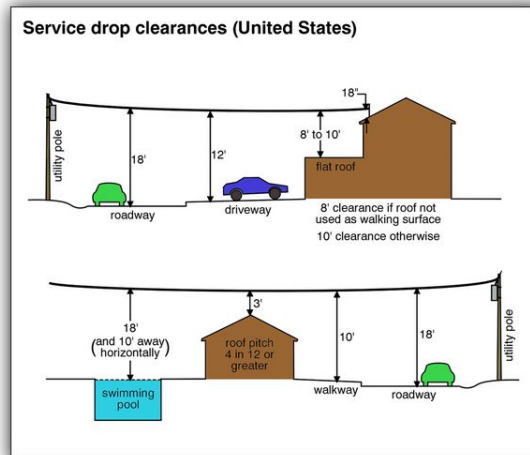

Grounding / Bonding

All components were found to be performing and in satisfactory condition on the day of the inspection.

-

B. Branch Circuits, Connected Devices, and Fixtures

Type of Wiring: Copper

Comments:

Receptacle Outlets

All components were found to be performing and in satisfactory condition on the day of the inspection.

Switches

All components were found to be performing and in satisfactory condition on the day of the inspection.

Fixtures

All components were found to be performing and in satisfactory condition on the day of the inspection.

Smoke Alarms

- There are no smoke alarms located in the home. Under current building standards, there should be a smoke alarm located in each sleeping room, outside each separate sleeping area in the immediate vicinity of the sleeping rooms, and on each additional story of the dwelling, including basements but excluding crawl spaces and uninhabitable attics (in dwellings with split levels and without an intervening door between the levels, a smoke alarm installed on the upper level and the adjacent lower level shall suffice provided that the lower level is less than one full story below the upper level).
- Note:** It is recommended to test for proper operation monthly and replace the batteries in all of the smoke detectors once a year for reasons of safety.

Carbon Monoxide Alarms

- I was unable to locate a carbon monoxide alarm in the immediate vicinity of the bedrooms.

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I NI NP D

III. HEATING, VENTILATION AND AIR CONDITIONING SYSTEMS

A. Heating Equipment

Type of System: Central Heating System

Energy Source: Gas




Brand Name: Ducane

Comments:

This component appears to be performing adequately at the time of this inspection. It is achieving an operation, function, or configuration consistent with accepted industry practices for its age.

Additional Observations and/or Comments:

- The gas supply flex connector was observed to be passing through the heating unit cabinet. Under current mechanical installation standards, this is no longer an accepted practice. Only rigid black gas pipe is allowed to pass through the heating unit cabinet.
- The heating unit flue (vent pipe) has inadequate clearance from combustible materials. Double walled vent pipes should have at least 1-inch of clearance and single walled vent pipes should have at least 6-inches of clearance from combustible material.
- There was a gas leak detected at or around the gas flex connector. The inspector used a gas leak detector to locate the leak.

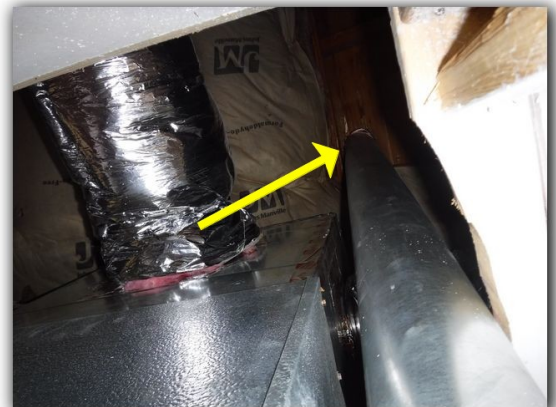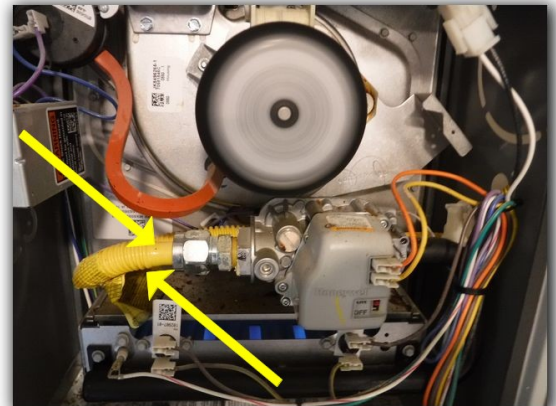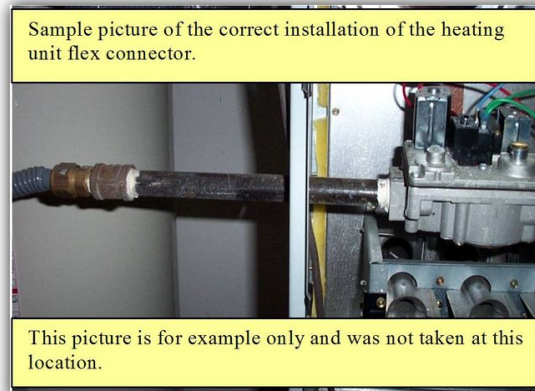

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I NI NP D

B. Cooling Equipment

Type of System: **Central Cooling System**

Today's Temperature Differential (Delta-T): **Unable to check Degrees**

Approximate System Age: **2016**

Approximate System SEER: **Unable To Determine**

Approximate System Size: **3 ton**

Filter Size: **20 x 20** Location: **Interior Wall Mounted**

Brand Name: **Ducane**

Comments:


The operation of the cooling system was not checked due to the outside ambient temperature being below 60 Degrees. If any concerns exist about the future operation of the cooling equipment, then it is recommended that a Qualified HVAC Technician further inspect and give an evaluation on the operation of the equipment and any further concerns that may exist with this equipment.

At this time, a limited visual survey will be performed and if any defects are found they will be listed in this section.

Additional Observations and/or Comments:

- The electrical service disconnect is installed behind the outside condenser/coil. This does not meet the clearance requirements of the National Electrical Code or the International Residential Code and should be corrected as necessary.
- Improper material is being used for the condensate drain line at this time. The condensate drain line should be made of an approved material (i.e. PVC or Ridged Insulated Copper) and be a minimum of 3/4 inch in diameter.
- **Note:** The primary condensate drain line is terminated next to the exterior foundation perimeter beam. It is recommended that the drain line terminate further away from the foundation beam or to an approved waste system.

Notice: Temperature differential readings are a fundamental standard for testing the proper operation of the cooling system. The normal acceptable range is considered approximately **between 15 to 23 degrees F.** total difference between the return air and supply air. Unusual conditions such as excessive humidity, low outdoor temperatures, and restricted airflow may indicate abnormal operation even through the equipment is functioning basically as designed and occasionally may indicate normal operation in spite of an equipment malfunction.

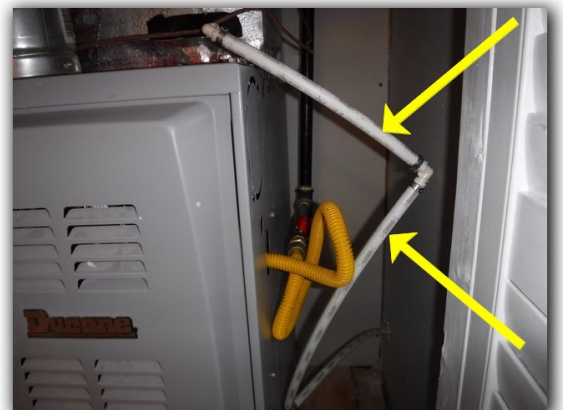

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I	NI	NP	D
---	----	----	---

C. Duct Systems, Chases, and Vents

Comments:

All components were found to be performing and in satisfactory condition on the day of the inspection.

IV. PLUMBING SYSTEMS

A. Plumbing Supply, Distribution Systems and Fixtures

Location of water meter: Within 5-feet of Front Curb

Location of main water supply valve: Within 3-feet of south exterior wall.

Static water pressure reading: 60 to 70 psi

Comments:

Water Supply System

All components were found to be performing and in satisfactory condition on the day of the inspection.

Exterior Faucets/Fixtures

All components were found to be performing and in satisfactory condition on the day of the inspection.

Laundry Connections

All components were found to be performing and in satisfactory condition on the day of the inspection.

Kitchen Sink

All components were found to be performing and in satisfactory condition on the day of the inspection.

Hall Bathroom

All components were found to be performing and in satisfactory condition on the day of the inspection.

Master Bathroom

All components were found to be performing and in satisfactory condition on the day of the inspection.

B. Drains, Wastes, and Vents

Comments:

All components were found to be performing and in satisfactory condition on the day of the inspection.

- **Note:** While water was run down the drains, this cannot simulate the waste flows characteristics of a fully occupied structure. Unless specified, fixtures and vessels were not filled to capacity for leak testing to prevent inadvertent water damage to the property. This means that some leaks may go undetected. Comprehensive water leak testing, including hydrostatic testing, may be available from qualified, licensed plumbers. You may also consider further testing and inspection of the sewer line(s) in older homes (40+ years), homes with previous foundation repair, and homes with evidence of poor foundation performance.

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I NI NP D



C. Water Heating Equipment

Energy Source: Gas

Capacity: 50 Gallons

Location: Interior Closet

Approximate Age: 2016

Brand Name: Whirlpool

Comments:

This component appears to be performing adequately at the time of this inspection. It is achieving an operation, function, or configuration consistent with accepted industry practices for its age.

Additional Observations and/or Comments:

- There is a rotten egg smell present when the hot water side of the plumbing fixtures are operated. It is recommended to flush the plumbing system and water heater and to check the condition of the anode rod in the water heater. If the anode rod is in poor condition, it is recommended to replace it.
- The vent pipe is not properly mounted at the top of the water heater. This configuration will emit Carbon Monoxide into the heater compartment, which is a known safety hazard.
- The water heater vent pipe is separated in the closet. This configuration will emit Carbon Monoxide into the closet area, which is a known safety hazard.
- There is no temperature and pressure relief valve (TPR) discharge pipe in place at the time of this inspection. For safety reasons, it is recommended that a TPR valve discharge pipe be installed. Under current building standards, the discharge pipe should run downward to the exterior of the structure, turn downward, and terminate within 6-inches of the ground.

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I NI NP D



D. Hydro-Massage Therapy Equipment

Comments:

E. Gas Distribution Systems

Comments:

Movement was detected in the gas gauge at the time of the gas check. This indicates a gas leak is present and needs to be investigated and repaired as necessary by a Qualified Licensed Plumber. The observation made to support the rendering of this opinion are listed but not limited to the following:

- There was a gas leak detected at the heating (HVAC) equipment. The inspector used a gas leak detector to locate the leak. This condition needs to be corrected for reason of safety.



F. Other

Comments:

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I NI NP D


V. APPLIANCES

A. Dishwashers

Comments:

Brand Name: Frigidaire

- The dishwasher drain hose is not properly installed to prevent back flow or anti-siphoning. It is recommended that an air gap device or high drain loop be installed in the drain line which can usually be accomplished without any expense as in Method-2 below.

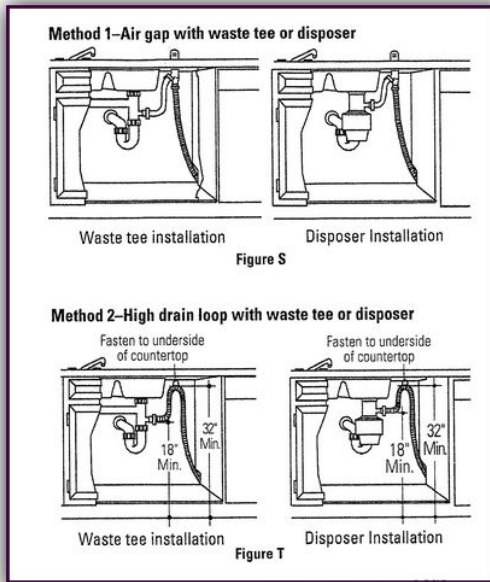

B. Food Waste Disposers

Comments:

Brand Name:

C. Range Hood and Exhaust Systems

Comments:

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I NI NP D

D. Ranges, Cooktops, and Ovens

Comments:

Range Brand Name: Samsung

This component appears to be performing adequately at the time of this inspection.

The oven was set to 350 degrees. When tested, at least 30 minutes later, the temperature rose to 350 degrees and held that temperature. A +/- of 25 degrees is considered acceptable.

Additional Observations and/or Comments:

- The range can be easily tipped over and should be equipped with an anti-tip device, for safety.

ANTI-TIP DEVICE

⚠ WARNING — To reduce the risk of tipping, the appliance must be secured by properly installed Anti-Tip bracket packed with this appliance.

If the Anti-Tip device supplied with the range does not fit this application, use the universal Anti-Tip device WB2X7909.




⚠ WARNING —

- All ranges can tip
- Injury to persons could result
- Install Anti-Tip bracket packed with range
- See Installation Instructions

If you pull the range out and away from the wall for any reason, make sure the Anti-Tip bracket is engaged when the range is pushed back against the wall.

9 ANTI-TIP DEVICE INSTALLATION

An **Anti-Tip bracket** is supplied with instructions for installation in a variety of locations. The instructions include all necessary information to complete the installation. Read the **Safety Instructions** and the instructions that fit your situation before beginning installation.



Typical installation of anti-tip bracket attachment to wall

⚠ WARNING:

- Range must be secured by **Anti-Tip bracket** supplied.
- If the Anti-Tip device supplied with the range does not fit this application, use the universal Anti-Tip device WB2X7909.
- See instructions to install (supplied with bracket).
- Unless properly installed, the range could be tipped by stepping or sitting on the door. Injury may result from spilled hot liquids or from the range itself.

E. Microwave Ovens

Comments:

Brand Name:

F. Mechanical Exhaust Vents and Bathroom Heaters

Comments:

G. Garage Door Operators

Comments:

I=Inspected

NI=Not Inspected

NP=Not Present

D=Deficient

I	NI	NP	D
----------	-----------	-----------	----------

H. Dryer Exhaust Systems

Comments:

This component appears to be performing adequately at the time of this inspection.

I. Other

Comments:
